

Bruce Freeman Rail Trail

Phase 2

Acton & Concord, MA

Acton DEP File# 85-1259 Concord DEP File# 137-1474

Chapter 91 Waterways Application# W18-5419 License# 15028

Week 2

This report entails the second week of work at the Bruce Freeman Rail Trail Phase 2 in Acton and Concord, MA for July 06, 2020 through July 10, 2020. Cobb was on site continuing to clear, remove cut material from the rail trail and started to pull small stumps.

**July 09, 2020**

Weather: KMAWESTA3 High of 93.2, sunny

Construction Observations:

- Removal of cut material within Acton.
- Chipping material in Acton.

Resource Areas:

- Removal of material from either side of the stream in Acton at station 22+00.

Action Items


- Need to install temporary erosion controls on either side of the stream in Acton at station 22+00. MON will be installing permanent erosion controls at a later date.

**July 10, 2020**

Weather: KMAWESTA3 High of 85.3, partly cloudy, 0.18" of rain after 6pm

Construction Observations:

- Removal of cut material within Acton outside resource areas.
- Chipping material in Concord.



- Removal of cut material in Concord from Nashoba Brook to outside the resource areas.

Resource Areas:

- Removal of cut material in Concord from Nashoba Brook to outside the resource areas.

Action Items

- Installation of temporary erosion controls, in the form of silt fence, on either side of the stream in Acton at station 22+00. MON will be installing permanent erosion controls at a later date.


The next work scheduled is chipping and grinding within Acton and Concord. If you have any questions please do not hesitate to contact me.

Sincerely,

Julia Fiske

413-625-6375

[jmfiskeenvironmental@yahoo.com](mailto:jmfiskeenvironmental@yahoo.com)



# Bruce Freeman Rail Trail Phase 2

## Week 2

### Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 09, 2020  
Removal of material from the stream in Acton at Station 22+00. Photo looking due north.



July 09, 2020  
Removal of material from the stream in Acton at Station 22+00. Photo looking due east.



# Bruce Freeman Rail Trail Phase 2


## Week 2

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 09, 2020  
Removal of material from the stream in Acton at Station 22+00. Photo looking due south.

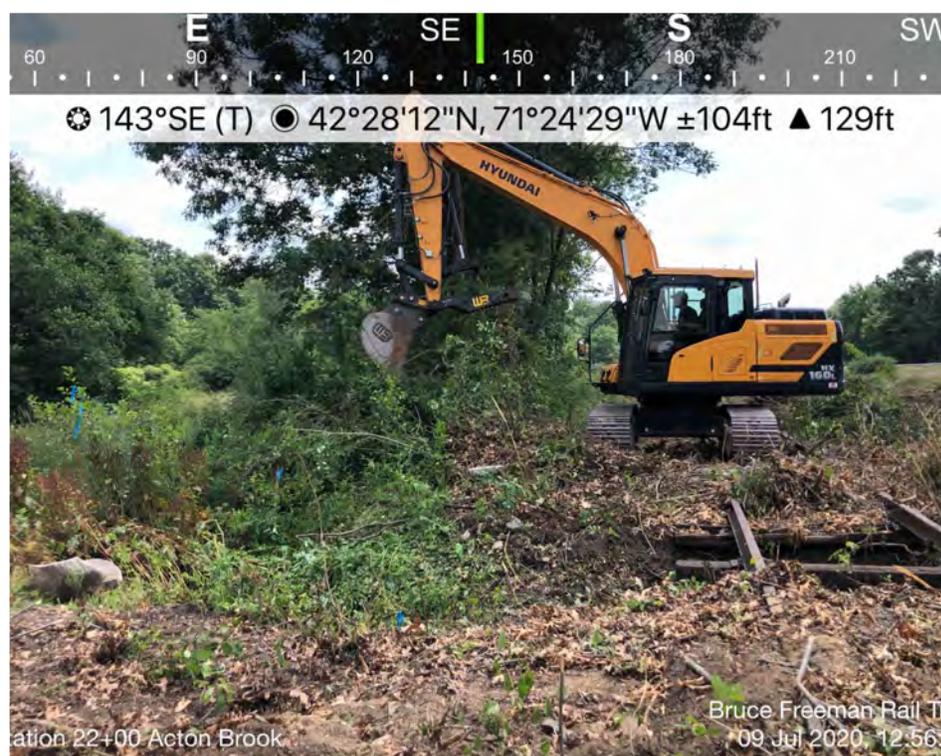

July 09, 2020  
Removal of material from the stream in Acton at Station 22+00. Photo looking due southeast.



## Bruce Freeman Rail Trail Phase 2

Week 2

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 10, 2020  
Looking at the stream in Acton  
at station 22+00 with temporary  
erosion controls. Photo looking  
due west.



July 10, 2020  
Looking at the stream in Acton  
at station 22+00 with  
temporary erosion controls.  
Photo looking due southeast.



JM Fiske Environmental

## Bruce Freeman Rail Trail Phase 2

Week 2

Acton & Concord, MA

Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 10, 2020  
Looking at the Nashoba Brook  
in Concord from the east side to  
the west side. Photo looking  
due northwest.



July 10, 2020  
Looking downstream at the  
east side of the Nashoba Brook  
in Concord at the cleared area.  
Photo looking due sotheast.
