

## Bruce Freeman Rail Trail

### Phase 2

### Acton & Concord, MA

Acton DEP File# 85-1259 Concord DEP File# 137-1474

Chapter 91 Waterways Application# W18-5419 License# 15028

### Week 3

This report entails the third week of work at the Bruce Freeman Rail Trail Phase 2 in Acton and Concord, MA for July 13, 2020 through July 17, 2020. Cobb remains on site chipping and stump grinding. Additional temporary erosion controls were installed in Concord within Nashoba River wetland resource areas.

#### **July 13, 2020**

Weather: KMAWESTA3 High of 88.5, mostly sunny. Rain 0.10 inches after 6pm.

#### Construction Observations:

- Removal of material within Acton and Concord.
- Chipping material in Acton.

#### Resource Areas:

- Removal of material from either side of the stream in Acton at station 22+00.
- Removal of cut material from either side of the Nashoba Brook in Concord.

#### Action Items


- Readjust erosion controls on either side of the stream in Acton at station 22+00. MON will be installing permanent erosion controls at a later date.

#### **July 14, 2020**

Weather: KMAWESTA3 High of 83.3, partly cloudy

#### Construction Observations:

- Stump grinding on the east side and west side of the Nashoba Brook.
- Stump grinding on the east side of the brook in Acton.



- Chipping in Acton

Resource Areas:

- Stump grinding on the east side and west side of the Nashoba Brook.
- Stump grinding on the east side of the brook in Acton.

Action Items

- Need to install temporary erosion controls within resource areas associated with Nashoba Brook in Concord. MON will be installing permanent erosion controls at a later date.

**July 15, 2020**

Weather: KMAWESTA3 High of 77.7, partly cloudy

Construction Observations:

- Stump grinding on the north side of the brook in Acton.
- Chipping in Acton.
- Installation of temporary erosion controls within resources areas of the Nashoba Brook.

Resource Areas:

- Stump grinding on the north side of the brook in Acton.
- Installation of temporary erosion controls within resources areas of the Nashoba Brook.

Action Items


- Installation of temporary erosion controls within resources areas of the Nashoba Brook. MON will be installing permanent erosion controls at a later date.

**July 16, 2020**

Weather: KMAWESTA3 High of 77.4, mostly sunny

Construction Observations:

- Stump grinding on the north side of the brook in Acton.
- Started pulling rail tracks in Concord outside of resource areas.
- Chipping in Acton.



JM Fiske Environmental

Resource Areas:

- Stump grinding on the north side of the brook in Acton.

Action Items

- None today

The next work scheduled is installation of permanent erosion controls in Acton and Concord. MIG will continue to pull railroad tracks within Concord. If you have any questions please do not hesitate to contact me.


Sincerely,

A handwritten signature in black ink that reads "Julia Fiske". The signature is written in a cursive, flowing style.

Julia Fiske

413-625-6375

[jmfiskeenvironmental@yahoo.com](mailto:jmfiskeenvironmental@yahoo.com)



# Bruce Freeman Rail Trail Phase 2

## Week 3

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 13, 2020  
 Removal of small stumps from the east side of Nashoba Brook on the north side of the rail trail in Concord. Photo looking due southeast.



July 13, 2020  
 Removal of small stumps from the east side of Nashoba Brook on the south side of the rail trail in Concord. Photo looking due west.



## Bruce Freeman Rail Trail Phase 2

Week 3

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 13, 2020  
Erosion controls to either side of the stream in Acton at Station 22+00 healed in again. Photo looking due southwest.



July 13, 2020  
Cleared trail in Acton, outside of resource areas, at station 09+45. Photo looking due south.



# Bruce Freeman Rail Trail Phase 2


## Week 3

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 14, 2020  
 Stump grinding from the east side of Nashoba Brook on the south side of the rail trail in Concord. Photo looking due west.

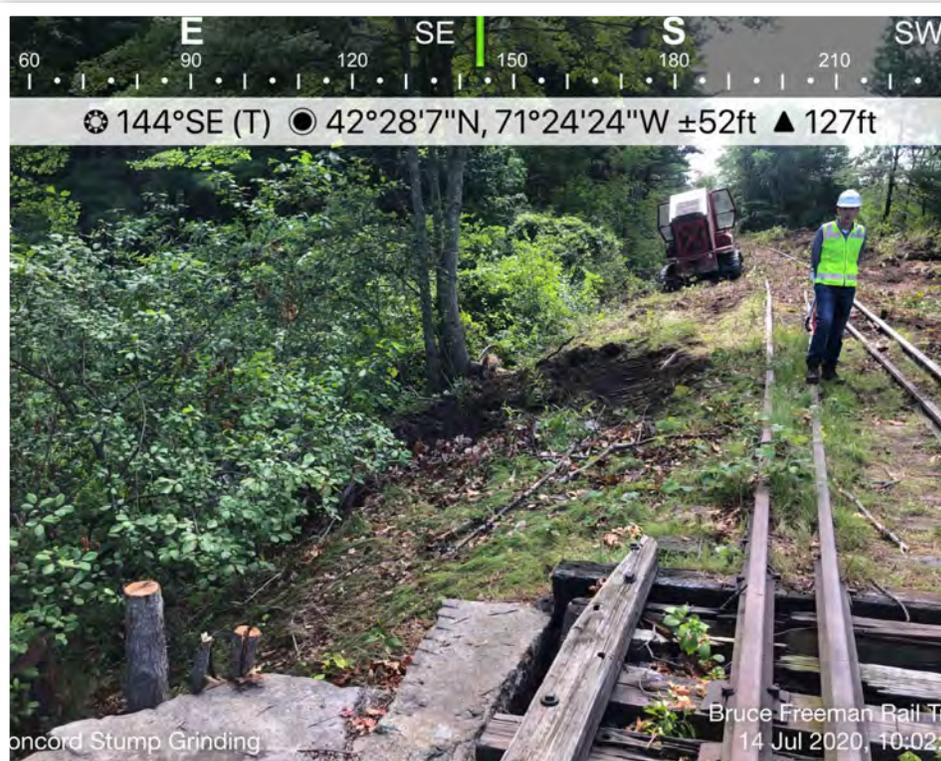

July 14, 2020  
 Stump grinding from the east side of Nashoba Brook on the north side of the rail trail in Concord. Photo looking due southeast.



## Bruce Freeman Rail Trail Phase 2

Week 3

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 14, 2020  
Stump grinding from the east side of Acton Brook on the north side of the rail trail in Acton. Photo looking due southeast.



July 15, 2020  
Grinding on the west side of the rail trail on the north side of the brook in Acton. Photo looking due north.



## Bruce Freeman Rail Trail Phase 2

Week 3

Acton & Concord, MA

Acton DEP File# 85-1259 Concord DEP File# 137-1474




July 15, 2020

Installation of temporary erosion controls in Concord to the east of Nashoba Brook and to the south of the rail trail. Photo looking due southwest.



July 15, 2020

Installation of temporary erosion controls in Concord to the east of Nashoba Brook and to the north of the rail trail. Photo looking due southeast.



## Bruce Freeman Rail Trail Phase 2

Week 3

Acton & Concord, MA

Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 16, 2020  
Rail Trail on the Acton side  
completely stumped. Photo  
looking due north.



July 16, 2020  
Work on the Acton side  
completely stumped. Photo  
looking due north.
