

Bruce Freeman Rail Trail

Phase 2

Acton & Concord, MA

Acton DEP File# 85-1259 Concord DEP File# 137-1474

Chapter 91 Waterways Application# W18-5419 License# 15028

Week 1

The first full week of work occurred at the Bruce Freeman Rail Trail Phase 2 in Acton and Concord, MA June 26 through July 02, 2020. Cobb was on site clearing the rail trail from Concord into Acton starting June 26, 2020 through July 01, 2020. Material was removed from the immediate proximity of the stream in Acton and the Nashoba Brook by July 01, 2020 days end. July 02, 2020 Cobb placed cut material into stock piles for chipping and grinding at a later date. No one from JM Fiske was on site July 02, cut material was being stock piled, for future processing, outside of any wetland resource area. No work occurred July 03, 2020.

June 26, 2020

Weather: KMAWESTA3 High of 88.6, sunny

Construction Observations:

- Clearing within Concord from the Nashoba Brook due southeast.

Resource Areas:


- Clearing within the resource areas of Nashoba Brook and the adjacent BVW.

June 29, 2020

Weather: KMAWESTA3 High of 72.1, overcast with 0.12" and 0.42" of rain from yesterday

Construction Observations:

- Finish Clearing within Concord from the Nashoba Brook to station 55+20.
- Start clearing within Acton from station 8+75 to approximately station 16+00.



June 30, 2020

Weather: KMAWESTA3 High of 75.4, sunny to cloudy 0.03" of rain

Construction Observations:

- Clearing within Acton from station approximately station 16+00 to station 20+00.

Resource Areas:

- Clearing within the resource areas of an unnamed stream at station 22+00 in Acton. No crossing of the stream was permitted. Trees cut were stacked approximately 25' from the bank.

July 01, 2020

Weather: KMAWESTA3 High of 80.1, sunny to cloudy

Construction Observations:

- Clearing within Acton from station approximately station 20+00 to station 25+00.
- Clearing within Concord from station 28+00 to 29+00.
- Removal of cut material to stock piles for processing at a later date.

Resource Areas:

- Clearing within the resource area of the west side of Nashoba Brook. Trees cut were stacked approximately 25' from the bank.


The next work scheduled is chipping and grinding. It is not certain when this will happen, it may be next week or the week after next. If you have any questions please do not hesitate to contact me.

Sincerely,

Julia Fiske

413-625-6375

jmfiskeenvironmental@yahoo.com



Bruce Freeman Rail Trail

Phase 2

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



June 26, 2020
Clearing on the northwest side
of the bridge over the Nashoba
brook in Concord. Photo
looking due northwest.



June 26, 2020
Clearing on the southeast side
of the bridge over the Nashoba
brook in Concord. Photo
looking due SSE.



Bruce Freeman Rail Trail

Phase 2

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



June 29, 2020
Clearing within the Acton portion of the rail trail near station 13+00. Photo looking due south.



June 29, 2020
Clearing in Acton station 15+00. Photo looking due NW.



Bruce Freeman Rail Trail

Phase 2

Acton & Concord, MA


Acton DEP File# 85-1259 Concord DEP File# 137-1474



June 30, 2020
Looking at the stream in Acton
at station 22+00. Photo looking
due south.



July 01, 2020
Trees cleared and removed
from the west side of the
Nashoba Brook. Photo looking
due NW.



Bruce Freeman Rail Trail

Phase 2


Acton & Concord, MA

Acton DEP File# 85-1259 Concord DEP File# 137-1474



July 01, 2020

Looking downstream of the Nashoba Brook in Concord at the cleared area. Photo looking due south.

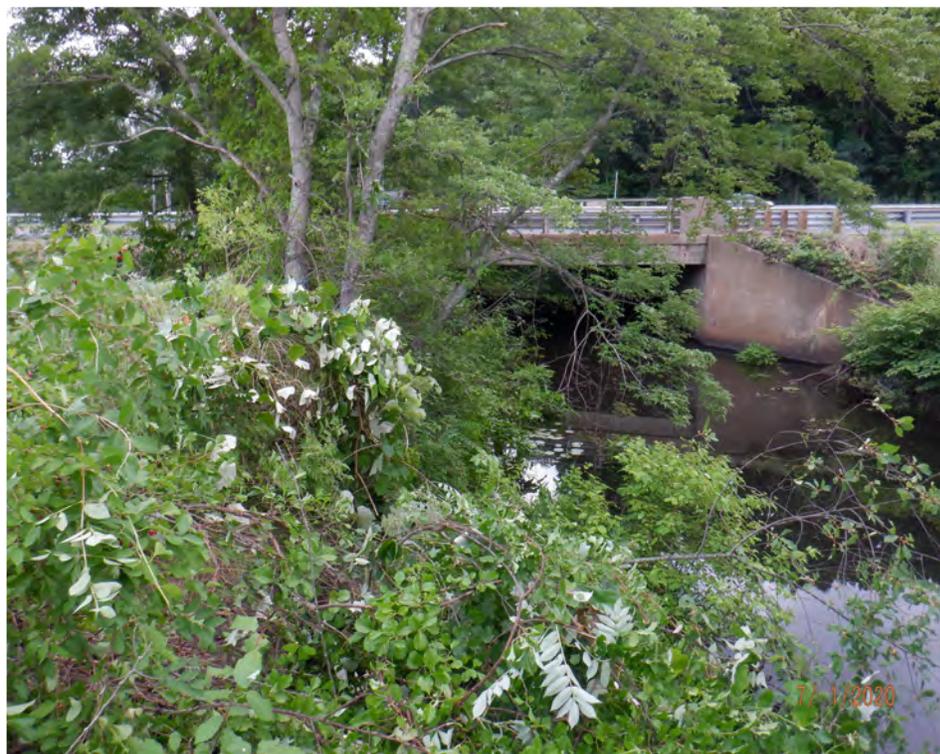

July 01, 2020

Looking upstream of the Nashoba Brook in Concord at the cleared area. Photo looking due NNE.
