

Construction Status

Phase I: J. Tropeano, Inc.

- Bid June 2018; commenced work September 2018
- Original Scheduled Completion: December 2019
- Current Status
  - Work Area 1 Completed: water main, underground conduit, drainage, binder pavement, curbing, stone walls & partial sidewalk
  - Work Area 3 Completed: water main, underground conduit, binder pavement & stone walls
  - Work Area 1 Remaining: relocate overhead utilities, complete sidewalks, brick crossings, final paving & landscaping
  - Work Area 3 Remaining: complete drainage, curbing, sidewalks, final paving & landscaping



Construction Status

Phase I: J. Tropeano, Inc.

- Current Scheduled Completion: Spring 2020
- Phase I Delays: National Grid & Overhead Utilities
  - NG Employee lockout June 2018 – December 2018
  - Delays with gas main construction: two distribution mains and the high-pressure transmission main
  - Relocation of overhead utilities to underground



Construction Status

Phase II: George Cairns & Sons, Inc.

- Original Scheduled to commence in December 2018, complete Phase II work in 2019
- Bid authorization November 2018; commenced work March 2019 after bid dispute
- Two season construction schedule presented in February 2019, w/ bridge open in October 2019, & Crosby Culverts done April 2020 – August 2020



Construction Status

Phase II: George Cairns & Sons, Inc.

- Current Status of Phase II Work
  - Work Area 2 Completed: partial water main, bridge, retaining walls, utility conduits, drainage, roadway construction, binder pavement

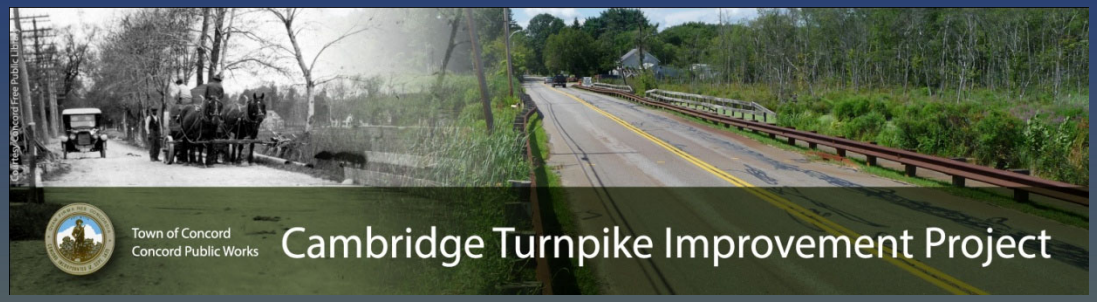

Construction Status

Phase II: George Cairns & Sons, Inc.

- Current Scheduled Completion
  - Bridge open May 2020
  - Work area 4 (Crosby) August 2020
- Phase II Delays
  - Delayed start of Deep Ground Improvements (impacted by Verizon)
  - Delayed start and slow initial progress of bridge construction
